


ID	Resource Names	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Sep '24							Oct '24							Nov '24							Dec '24							Jan '25						
								19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	02	09	16	23	30		
1			<b>Balcony Sequence</b>	<b>64 days</b>	<b>Wed 04/09/24</b>	<b>Mon 02/12/24</b>		[Gantt bar for Balcony Sequence from Sep 04 to Dec 02]																																		
2	Concrete Mounting Crew		Inner Leaf.	9 days	Wed 04/09/24	Mon 16/09/24		[Gantt bar for Concrete Mounting Crew from Sep 04 to Sep 13]																																		
3	Concrete Mounting Crew		Fixed Prefabricated Balcony Rail	1 day	Tue 17/09/24	Tue 17/09/24	2	[Gantt bar for Concrete Mounting Crew from Sep 13 to Sep 13]																																		
4	Brick layer		Insulation + Brick Work (ladders)	14 days	Thu 31/10/24	Tue 19/11/24	3	[Gantt bar for Brick layer from Oct 31 to Nov 14]																																		
5	Balcony Mounting Crew		Placing the Balcony Steel Frame on the bottom rail.	1 day	Wed 20/11/24	Wed 20/11/24	4	[Gantt bar for Balcony Mounting Crew from Nov 20 to Nov 20]																																		
6	Balcony Mounting Crew		Bolting the Stag on the top Balcony rail.	1 day	Thu 21/11/24	Thu 21/11/24	5,4	[Gantt bar for Balcony Mounting Crew from Nov 21 to Nov 21]																																		
7	Balcony Mounting Crew		Temporarily OSB board cover.	1 day	Fri 22/11/24	Fri 22/11/24	6	[Gantt bar for Balcony Mounting Crew from Nov 22 to Nov 22]																																		
8	Balcony Mounting Crew		Connecting the downpipe to the balcony steel frame	1 day	Mon 25/11/24	Mon 25/11/24	7	[Gantt bar for Balcony Mounting Crew from Nov 25 to Nov 25]																																		
9	Balcony Mounting Crew		Mix of Elastic Sealant with Sand between the balcony steel frame and the bricks	1 day	Mon 25/11/24	Mon 25/11/24	7	[Gantt bar for Balcony Mounting Crew from Nov 25 to Nov 25]																																		
10	Balcony Mounting Crew		Bottom part and Fascia board fixed on the steel frame. (Using the Forklift with the Basket)	1 day	Tue 26/11/24	Tue 26/11/24	8	[Gantt bar for Balcony Mounting Crew from Nov 26 to Nov 26]																																		
11	Balcony Mounting Crew		Brick Elastic Joints	1 day	Wed 27/11/24	Wed 27/11/24	10	[Gantt bar for Balcony Mounting Crew from Nov 27 to Nov 27]																																		
12	Balcony Mounting Crew		Wooden Studs screwed in the Steel profile for the floor.	1 day	Wed 27/11/24	Wed 27/11/24	10	[Gantt bar for Balcony Mounting Crew from Nov 27 to Nov 27]																																		
13	Balcony Mounting Crew		Floor - Fiber Cement Planks	1 day	Thu 28/11/24	Thu 28/11/24	12	[Gantt bar for Balcony Mounting Crew from Nov 28 to Nov 28]																																		
14	Balcony Mounting Crew		Steel Plate above the mortar 20mm for a better entrance and to cover everything.	1 day	Fri 29/11/24	Fri 29/11/24	13	[Gantt bar for Balcony Mounting Crew from Nov 29 to Nov 29]																																		
15	Balcony Mounting Crew		Glass Railing	1 day	Mon 02/12/24	Mon 02/12/24	14	[Gantt bar for Balcony Mounting Crew from Dec 02 to Dec 02]																																		

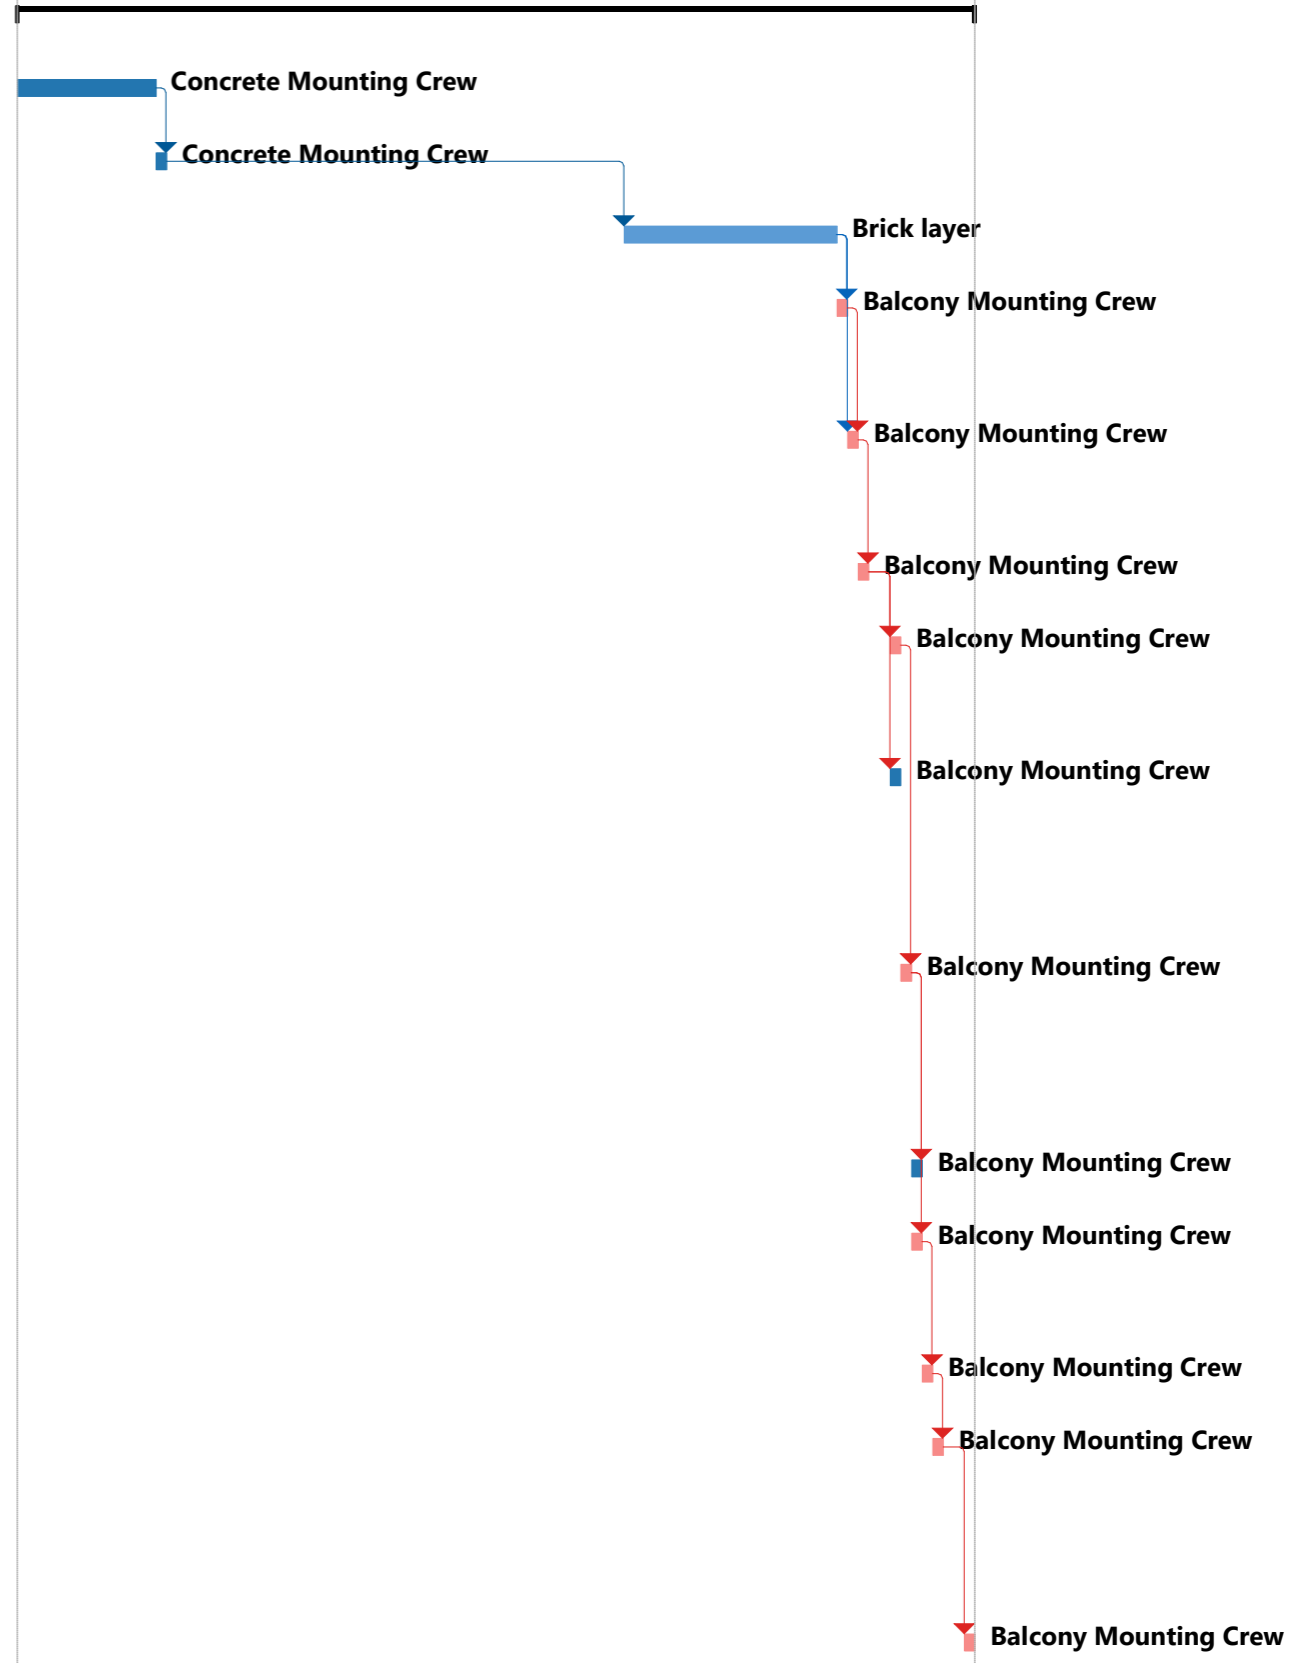

Project: MultiHall-Take1w  
Date: Mon 27/11/23

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
